

Pima County **BOND** PROGRAM *Update*



Semi-annual Report for Fiscal Year 2008/2009

Introduction

The 1997 General Obligation and Sewer Revenue bond authorization was reported substantially complete in June 2007. The capital improvement program continues with implementation of the three active bond authorizations: the 1997 Highway User Revenue Fund (HURF) bonds; 2004 General Obligation (GO) and Sewer Revenue bonds; and the 2006 GO bonds for the Psychiatric Hospital and Urgent Care Facilities. During the six months ending December 2008, there have been 34 projects and subprojects completed and two open space acquisitions totaling \$58.5 million. This update provides the progress of these bond authorizations at the end of December 2008.



Manuel Herrera Park Improvements

Financial Summary

Bond Authorization and Sales

The three active bond authorizations have had 14 bond sales, totaling \$734.5 million, leaving 35 percent of the bond authorizations remaining to be sold. The most recent bond sale of \$75 million Sewer Revenue bonds was in May 2008. The next sale is planned for March or April 2009: \$75 million GO bonds and \$28.9 million Sewer Revenue bonds. Revenue collected from secondary property taxes is used to pay off GO debt on issued bonds. Transportation revenue bonds are issued and repaid with funds received from street and highway user revenues. Street and highway user revenues consist of taxes received from the State of Arizona's distribution of HURF funds from multiple sources, including the vehicle license tax, fuel tax, motor carrier fees and use taxes. Sewer revenue bonds are issued and repaid with sewer user and connection fees. For detailed financial information, please refer to the Comprehensive Annual Financial Report (CAFR) at: www.pima.gov/GenInfo/Budget.html.

Bond Sales

Bonds	Total Authorization (Million)	Total Bond Sales (Million)	Remaining Authorization (Million)	Percent Remaining
1997 General Obligation	\$257.0	\$236.4	\$20.6	8%
1997 Sewer Revenue	\$105.0	\$101.4	\$3.6	3%
1997 HURF Revenue	\$350.0	\$227.2	\$122.8	35%
2004 General Obligation	\$582.3	\$270.9	\$311.4	53%
2004 Sewer Revenue	\$150.0	\$124.7	\$25.3	17%
2006 General Obligation	\$54.0	\$10.3	\$43.7	81%
Total	\$1,498.3	\$970.9	\$527.4	35%

Pima County Board of Supervisors

Richard Elías, Chairman, District 5
 Ann Day, District 1
 Ramón Valadez, District 2
 Sharon Bronson, District 3
 Raymond J. Carroll, District 4


Pima County Administrator

Chuck Huckelberry

Pima County Bond Advisory Committee Members

Larry Hecker, Chair
 Carolyn Campbell, Vice Chair
 Peter Backus
 Pat Benchik
 Gary Davidson
 Pete Delgado
 Paul Diaz
 René Gastelum
 Harry George
 Jesus Gomez
 Kelly Gomez
 Byron Howard
 Terri Hutts
 David Lyons
 Rebecca Manoleas
 A.C. Marriotti
 Wade McLean
 John Neis
 Ted Prezelski
 Patty Richardson
 Chris Sheafe
 Thomas Six
 Dan Sullivan
 Tom Warne
 Greg Wexler

1997 HURF Revenue Bond Authorization



1997 HURF Revenue Bonds	Authorization
Total HURF Revenue Bonds	\$350 million
Less RTA Projects Allocation	\$50 million
Balance for Bond Program	\$300 million

Summary

The 1997 HURF bond authorization includes 58 projects with a bond authorization of \$350 million. With the approval of the Regional Transportation Authority (RTA) plan, nine of these projects with approximately \$50 million in bond authorization will now be included in the RTA status reports. Completion of these projects is contingent upon RTA funding and priorities. The remaining \$300 million in authorization consists of 47 site-specific projects and two multi-project programs. The

two multi-project programs, Transportation Safety and Neighborhood Transportation Improvements, have spent approximately 60 percent of the authorized bond funds and will continue to complete projects as funding allows. At the end of December 2008, 37 of the 47 site-specific projects or 79 percent are completed or under construction, 73 percent or \$218.1 million of the \$300 million bond authorization is spent.


Questions	Site-Specific Projects*	Completed/Construction	Design	Future
HURF Revenue Bonds	47	37	2	8

* Excludes program sub-projects and RTA projects

Future Projects*

Bond Number	Name	Bond Authorization
DOT-07	Orange Grove Road at Geronimo Wash	\$0.8 million
DOT-11	Drexel Road, Tucson Boulevard to Alvernon Way	\$6.5 million
DOT-23	Thornydale Road, Cortaro Farms Road to Linda Vista Blvd.	\$1.0 million
DOT-24	Mainsail Boulevard and Twin Lakes Dr, Twenty-Seven Wash	\$2.7 million
DOT-27	River Road at Ventana Wash	\$1.9 million
DOT-32	Kolb Road, Sabino Canyon Road to Sunrise Drive	\$10.0 million
DOT-44	Orange Grove Road, Thornydale Road to Oracle Road	\$20.0 million
DOT-53	Old Tucson-Nogales Highway-Summit Neighborhood	\$1.1 million

* Future meaning no formal activity is ongoing.

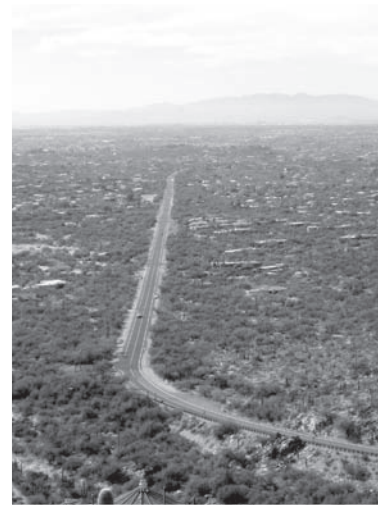

Catalina Highway


Regional Transportation Authority Projects (Supplemented by Bond Funds)

Bond Number	Name
DOT-06	Magee Road: La Cañada Drive to Oracle Road
DOT-10	La Cañada Drive, Ina Road to Calle Concordia
DOT-20	La Cholla Boulevard: River Road to Ruthrauff Road
DOT-28	Speedway Boulevard: Camino Seco to Houghton Road
DOT-29	Houghton Road: I-10 to Tanque Verde Road
DOT-31	Tanque Verde Road: Catalina Highway to Houghton Road
DOT-37	I-19 Frontage Rd: Continental Road to Canoa
DOT-40	Grant Road: Oracle Road to Swan Road
DOT-56	Broadway Boulevard: Euclid Avenue to Country Club



Craycroft Road

2004/2006 General Obligation and Sewer Revenue Bonds



Year	Bonds	Authorization
2004	General Obligation Bonds	\$582.25 million
2006	General Obligation Bonds	\$54 million
2004	Sewer Revenue Bonds	\$150 million

Summary

The 2004/2006 bond program will be completed over 12 years. The program includes 81 General Obligation and Sewer Revenue site-specific projects. In 2006, an additional \$54 million of General Obligation bonds were approved for the Psychiatric Urgent Care and Inpatient Hospital Facilities. In addition to the 81 site-specific projects, there are seven programs that will complete projects or acquisitions as identified. At the end of December 2008, 46 projects or 57 percent are either completed or under construction along with the acquisition of 55 open space properties. These projects and acquisitions, as well as projects in the design phase, have expended \$373 million or 47 percent of the total \$786.25 million in authorized bond funding.

Current Status

The 2004/2006 General Obligation and Sewer Revenue bond authorization has six questions and 81 projects*. Currently there are 46 projects completed or in construction, 27 in design and eight planned for future development. In addition to the construction project questions, Question 1 authorization is for open space, habitat protection, and prevention of Davis-Monthan Air Force Base encroachment. To date, there have been 55 completed acquisitions, leaving \$67.3 million remaining of the original \$174.3 million authorized for this question.



Avra Valley Clarifiers

Site-Specific Questions*	Site-Specific Projects**	Completed/ Construction	Design	Future***
2. Public Health, Community Facilities	13	8	2	3
3. Public Safety and Justice Facilities	7	5	1	1
4. Parks, Recreational Facilities	44	22	21	1
5. River Parks and Flood Control	8	5	2	1
6. Sewer System	9	6	1	2
Total	81	46	27	8

*Does not include Question 1, Open Space, Habitat Protection, Davis Monthan AFB Encroachment Prevention land acquisitions.

**Excludes program sub-projects.

***Future means no formal activity ongoing.

2004 Open Space Bond Program Status (Question 1)



Flowing Wells Health Clinic

Categories	Beginning Authorization	Number of Acquisitions	Remaining Authorization	Percentage Remaining
Community Open Space	\$37.3	15	\$17.0	46%
Jurisdictional Requests	\$15	4	\$12.1	81%
Habitat Protection Priorities	\$112	23**	\$35.9	32%
Davis-Monthan AFB Encroachment	\$10	13	\$2.3	23%
Total	\$174.3	55	\$67.3	39%

** \$18.9 million in additional funds for Sands Ranch and Sopori Ranch are scheduled for payment in the next fiscal year.

Current Highlights

1997 General Obligation and Sewer Revenue Bond Program

Although the 1997 General Obligation and Sewer Revenue Bond Programs were substantially complete in June 2007, there remains small portions of the programs that are dependent upon more favorable conditions and resolution of issues that impact project delivery. The remaining portions of the 1997 General Obligation and Sewer Revenue Bond Programs will continue to be highlighted in this portion of the update.



Columbus Park

Irvington to Valencia, Columbus Park, Thomas Jay Regional Park, and various trailhead staging areas and trail acquisitions. The following projects have been completed: Santa Cruz River Park Playgrounds, Rudy Garcia Park, Manual Herrera Park, and the Yes2Kids Handball Court. The Tucson Children's Museum is nearly complete.

Question 1 – Juvenile Detention and Court Facilities

Completed in 1998.

Question 2 – Public Safety, Law Enforcement and Superior Court

Completed in 2005.

Question 3 – Parks

Substantially complete: 86 percent of the parks projects are complete or under construction. The following projects are either under construction or will begin construction over the next year: two projects under the Athletic and Play Field Improvements program located in the City of Tucson, Rillito River Park-Campbell to Alvernon and at Columbus Blvd., Oro Valley Cañada del Oro River Park, Santa Cruz River Park-

Question 4 – Sonoran Desert Open Space and Historic Preservation: Open Space portion of Question 4:

Substantially complete: The County has purchased 23 properties totaling \$24.7 million. The remaining \$3.2 million will be spent on eligible properties as sellers are identified.

Cultural Resources and Historic Preservation portion of Question 4:

The 1997 Cultural Resources and Historic Preservation bond program is substantially complete, with the exception of one bond project involving the acquisition of State Trust Lands for Tumamoc Hill. This project totals \$1.3 million, which will be applied to the future auction by the Arizona State Land Department and sale of Tumamoc Hill to Pima County. Rehabilitation of the "Cowboy House" at Empirita Ranch was completed in December 2008, and exterior restoration of various buildings at Canoa Ranch were



Avra Valley WWTf General Site

completed by October 2008. Construction of the Anza National Historic Trail on the Canoa Ranch is complete.

Parks portion of Question 4:

The 1997 Trails portion of Question 4 has three projects completed. The remaining site-specific project, Tortolita Mountain Park Trail System Master Plan, is scheduled for completion by June 30, 2009. This will complete the Trails portion of the 1997 bond program.

Question 5 – Public Health, Safety, Recreational and Cultural Facilities

The Facilities portion is substantially complete: All site-specific projects have been completed, including the Marana Library Expansion.

Thirty-eight of the 41 approved 1997 Neighborhood Reinvestment projects have been completed, and the remaining three are projected to be finished before the end of FY2008/2009. The City Parkside lighting project is complete. The Sunset Villa traffic and lighting project is scheduled to be completed in March 2009. The Rancho Chukson project obtained a substantial change approval from the Board of Supervisors, and is projected to be completed by June 2009. Santa Rita Skate park has a projected completion date of March 2009.

The Housing Reinvestment Bond Program had nine affordable housing development proposals approved by the Board of Supervisors. The approved developments, when built-out, will result in a total of 262 new units of affordable housing. As of December 31, 2008, eight of the nine infrastructure development projects have been completed and the ninth project is in progress, resulting in 202 new units of affordable housing. An additional six homes were under construction at the end of the 2008 calendar year. Completed Projects and highlights for 2008:

- West Ochoa Project: Infrastructure was completed; all five homes were completed, sold and occupied by June 2008.
- Balboa-Laguna Habitat Houses: Project infrastructure, including a City-owned pocket park was completed in December 2008; all 36 homes have also been completed, sold and occupied.
- Copper Vista II, the ninth and final housing project

approved under the 1997 GO Program, started construction in December 2008.

- We-Chij Estates Project: While infrastructure was completed by the end of 2007, home construction did not start until 2008; 15 affordable homes have now been sold, completed and occupied. The remaining five affordable homes were under construction and expected to be completed and occupied during the first quarter of 2009.

Question 6 – Flood Control Improvements

Substantially complete: the flood control bond program is substantially complete with two projects remaining. One of the projects, FC-04 Mission View Detention Basin, consists of the integration of the detention basins, development of new mainline sanitary sewers, and future parks and recreational amenities with a major residential, commercial, and research community on Tucson’s south side. Construction on this project began in late August 2008, the storm drain pipes have been installed and the detention basin will be complete in April 2009. The second project, FC-02 Santa Cruz River Bank protection: Valencia to Irvington has been delayed by the United States Army Corps of Engineers due to limited Federal funds for non-military projects.

Question 7 – Solid Waste Improvements

The completion of the Solid Waste improvements is dependent on future funding. Pima County is evaluating alternatives to meet regional solid waste management needs in lieu of developing a new regional landfill.

Question 8 – Sewer System Revenue Bonds

The 1997 Sewer Revenue Bond Program is substantially complete with the exception of two remaining projects. The Tanque Verde Interceptor is moving forward by securing the application for the U.S. Army Corps of Engineers Section 404 permit, obtaining archeological clearance, and right-of-way acquisition. The second project involves the final phase of the Arivaca Junction Sewer Extension. The developer-related portion of this project is on hold due to market conditions.

1997 HURF Bond Program

In the past six months two DOT-57 Safety Improvement bond projects have started construction: Orange Grove/Silverbell Intersection and Sunset/Sunray Intersection. During this period three bond projects were in the final design stages and are expected to go to construction in the next six months: DOT-47, Sunrise Drive, Craycroft to Kolb; DOT-37, I-19 Northbound Frontage Road, and DOT-10, La Canada, Ina to Calle Concordia. These five projects have a combined total cost of \$73 million. Active design continued on two other major roadway bond projects: DOT-20, La Cholla, Ruthrauff to Ina; DOT-31, Tanque Verde, Catalina Highway to Houghton. Continuation of the design phase for DOT-50, Kinney Road, Ajo to Bopp is awaiting private developer decisions.



Sunrise Drive and Craycroft Road Intersection

2004/2006 General Obligation and Sewer Revenue Bond Program

Question 1 – Sonoran Desert Open Space and Habitat Protection; Prevention Urban Encroachment of Davis-Monthan Air Force Base

Under the Sonoran Desert Open Space and Habitat Protection portion of this question, Pima County has acquired 42 properties for a total of \$115.3 million, including 35,000 acres of land in fee and 127,000 acres of State grazing leases and Federal grazing permits. Two large ranches were acquired over the past six months. The Sopori Ranch acquisition included the 5,000 acres of fee land and 10,000 acres of State grazing leases east of Arivaca and south of Green Valley. This purchase expands a system of federal and County conservation reserves in the area, including the Coronado National Forest, the Buenos Aires National Wildlife Refuge, and the County's Rancho Seco. In doing so it preserves wildlife corridors in this area, as well as decreasing the threat to the Sopori Creek from groundwater pumping. The Sands Ranch acquisition included 5,000 acres of fee land in the far south eastern corner of Pima County, northeast of Sonoita. The acquisition contributes to an interconnected system of conserved lands from the Santa Rita Mountains, across the Las Cienegas National Conservation Area, to the Whetstone Mountains, protecting the health of the Cienega Watershed, high quality grasslands, and a very diverse intact ecosystem.

In addition, Pima County has spent \$7.6 million of the original \$10 million bond authorization to acquire 286 acres in 13 parcels to prevent urban encroachment near Davis-Monthan Air Force Base.


Question 2 – Public Health and Community Facilities (and 2006 Bond Authorization, Question 3 – Psychiatric Crisis Recovery Center and Question 4 – Psychiatric Inpatient Hospital Facilities)

The Green Valley Performing Arts Center Phase 2 is substantially complete. The Psychiatric Hospital and Crisis Recovery Center have received building permits and with Authorization to Proceed the project is ready to begin construction.

The 2004 Neighborhood Reinvestment portion of this question has 48 projects approved by the Board of Supervisors. Eighteen projects are complete: Miracle

Manor Milagro Playground, South Park Quincie Douglas swimming pool slide structure, Midvale street lighting, South Tucson mini parks, Oak Flower street lighting, Santa Catalina community center, Alvernon Heights traffic mitigation, Flowing Wells park improvements, Marana Vista sidewalks and street lighting, Ajo skate park, A Mountain sidewalks, Feldman's sidewalk project, Highland Vista park amenities, Flowing Wells health clinic, Julia Keen street lights, Rillito Neighborhood park improvements, Hedrick Acres public safety improvements, and Cardinal traffic mitigation enhancements. Nine projects are currently under construction and eighteen are in the planning and development stages. There are three projects pending approval of an Intergovernmental Agreement with various agencies and municipalities.

The 2004 Affordable Housing General Obligation funds are obligated for a total of \$10 million for 534 new units of affordable housing for low-income families. Ten development projects have been approved by the Pima County Board of Supervisors. As of December 31, 2008, a total of five development projects have been completed resulting in 101 new units of affordable housing. Five infrastructure projects including seven homes are under construction. Additionally, The Pima County Housing Commission recommended five new funding requests to the Board of Supervisors totaling \$5.3 million which will result in 281 new affordable housing units. These recommendations were approved by the Board of Supervisors at their January 13,

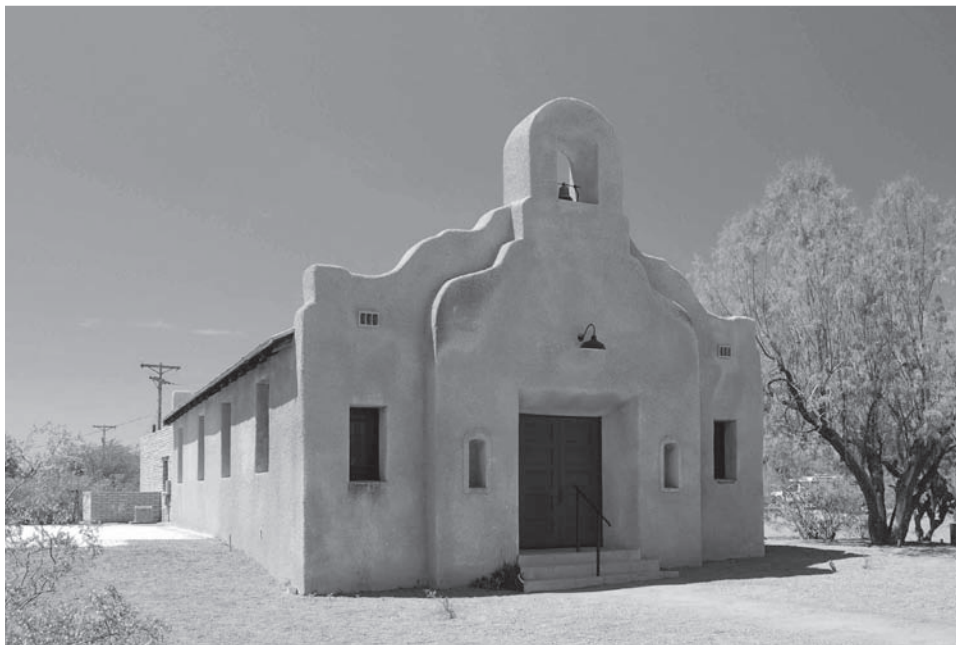

San Pedro Chapel

2009 meeting. Completed projects and Highlights for the 2008 calendar year include:

- Corazon Del Pueblo – Phase II Infrastructure is complete.
- Sylvester Drive Estates Infrastructure is complete. Construction of first 3 homes started in December 2008.
- Eight new Habitat homes at Corazon Del Pueblo Phase I are complete.
- One home constructed at Iowa Project (Chicanos Por La Causa) and one home constructed at the Barrio San Antonio Civano Demonstration Project also known as Lessons from Civano (Drachman Design Build Coalition).

The Ina Road Tire Facility Relocation project is on hold. The County is revising its tire management operations to eliminate tire storage and instead utilize a system for collection and rapid transfer to a recycling facility. Facility relocation may not be necessary.

Question 3 – Public Safety and Justice Facilities

The business planning process for the Pima County Wireless Integrated Network (PCWIN) project is completed. Approval of the PCWIN Business Plan culminated a lengthy planning process resulting in conceptual systems design and a business strategy for implementing and sustaining voice and data radio systems, and emergency communications and operations facilities. Nineteen

of the thirty-two participating agencies, representing greater than 90% of the future radio users have submitted memorandums of commitment indicating their continuing commitment to the project. Proposals for voice and data radio systems have been received and evaluated. The PCWIN Executive Management Committee has made a recommendation for award of contract for voice radio systems for Board of Supervisors consideration. The Committee further recommends reducing project scope by eliminating the mobile data system elements of the project. Their recommendation is based on an unfavorable cost benefit analysis. Architectural programming services for the dispatch and emergency operations center are nearing completion and will be immediately followed with architectural engineering design services. On behalf of the PCWIN project, the County has been awarded several federal grants totaling more than \$5 million.

The Juvenile Court build-out of new courtrooms, judges chambers, training center, and HVAC system upgrades is complete. The Corrections Jail Security consisting of seven projects is partially complete. The largest of these projects, the training center addition, is complete providing class and training space for corrections officer and deputy academy classes. The Interagency Advocacy Center was opened in October 2008 serving the advocacy of children in Pima County. The New Justice Court/Municipal Court Complex, at \$76 million, is in the design phase. Extensive archeology excavation and associated utility relocations are complete. Additional funding will be necessary for this project.

Question 4 – Parks and Recreational Facilities

Of the 26 parks projects, nine have been completed to date with eight additional projects to be completed or in construction in Fiscal Year 2008/2009. Nine other projects are currently in planning and design. One project managed by the Town of Marana is in construction.

The 2004 Cultural Resources and Historic Preservation portion of Question 4 furthers the objectives of the 1997 program and includes the acquisition of specific highly significant archaeological and historical sites and additional rehabilitation efforts at various historic sites. Since acquiring the 13-acre Honey Bee Village Hohokam site, the site has been fenced and signs will be installed to protect the site. Construction and rehabilitation of the Empirita Ranch “Cowboy House” was completed in November 2008. A master plan for Steam Pump Ranch has been completed, and stabilization efforts are in progress.

The Anza National Historic Trail is almost complete from Elephant Head Road north to Sahuarita, and signage for the trail will be installed in the near future. Exterior rehabilitation and restoration of Buildings 103, 105, 106, 107, 108 and 109 at Canoa Ranch are complete. Design of the exterior rehabilitation of Canoa Ranch Buildings 101, 102, 104, and 110 is underway. Clean-up of the site surface at the Fort Lowell Adkins parcel is complete. Emergency repairs and stabilization of Fort Lowell adobe Officers Quarters 1 and 2 and a cultural resources inventory survey of the Adkins property were completed between February



Tuquison Trailhead



Flowing Wells Basketball Court

and April 2008. Master planning for the entire Fort Lowell Park area is underway. Rehabilitation and other improvements at the San Pedro Chapel were completed in July 2008. Archaeological mapping and GIS database projects were completed at Dakota Wash and Los Morteros Conservation Areas in March and April 2008.

Two 2004 projects that are currently on-hold are the acquisition of the Helvetia Townsite and Marana Mound site. Funds from these projects have been made available for the future auction and purchase of Tumamoc Hill from the Arizona State Land Department planned for February 2009.

The libraries portion of this question authorizes \$12.6 million for three library projects. The Oro Valley and Marana Town library expansions and Marana Continental Ranch Library are complete. The Wilmot Library design is underway with construction scheduled for completion by fall 2010.



Performing Arts Center – Tucson

Question 5 – River Parks and Flood Control Improvements

Under Question 5 the County expended \$24.4 million of the \$46.2 million authorization by the end of the 2008 calendar year. Construction of the linear parks on the Cañada Del Oro at the Tucson Omni Golf Course should be substantially complete by early 2009 and the Rillito River between Craycroft and Alvernon should be substantially complete by April 2009. Construction of drainage improvements in the City of South Tucson are underway. Plans are being developed for construction in Fiscal Years 2009/10 and 2010/11 for the linear parks on the Cañada Del Oro from Thornydale to Magee and on the Santa Cruz River from Grant to Camino del Cerro respectively.

Question 6 – Sewer System Revenue Bonds

The Regional Wastewater Reclamation Department has nine site-specific projects and the Miscellaneous Conveyance System Rehabilitation and Repair underway. The three largest projects, the New Marana Wastewater Reclamation Facility Expansion, the Avra Valley Biological Nutrient Reduction Oxidation Ditch

(BNROD) Expansion, and the Santa Cruz Interceptor – Phase II are all in construction or nearing completion. A new 0.5 Mgd Biolac reclamation system at the Marana Wastewater Reclamation Facility (WRF) has been completed, including an Ultra Violet (UV) and Filtration system. The Biolac system was placed in service in spring/summer 2007 while UV/Filtration disinfection system was operational in October 2008. The construction of a new 4.0 Mgd BNROD reclamation facility at the Avra Valley WRF is underway with anticipated completion in summer 2009, which

is ahead of schedule and within budget. The Santa Cruz Interceptor—Phase II sewer is anticipated to be placed in service early spring 2009. The project was completed ahead of the original schedule. Additionally, work efforts associated with Rehabilitation and Odor Control at the Roger Road WRF are substantially complete. These rehabilitation efforts included installation of a new storm water retention

basin, rehabilitation of the existing storm water retention basin,

installation of a new gravity belt thickener, electrical upgrades, new methane gas compressing system, and installation of full containment systems for chlorine and bisulfate storage. The odor control projects included covering the head works, primary clarifier weirs, collection of the emissions from the bio-towers, and upgrading handling of the biosolids odors. All odor work was completed in 2007 and 2008. The initial phase of the Regional Optimization Master Plan (ROMP) study has been completed. The next phase for the design portions for the nutrient removal facility and process upgrade at the Ina Road WPCF was awarded in 2008. The design consultant and the construction manager for the Santa Cruz Interceptor-Phase IV (Plant Interconnect) have been selected, the design is complete. Construction is scheduled to commence in the spring of 2009. Finally, the first portion of the Mount Lemmon Wastewater Master Plan has been completed, and design of an equalization tank with improved influent solids handling will be awarded in the spring of 2009 along with a separate contract to line portions of the existing collection system to reduce inflow.

This update is a snapshot of the program as of December 2008. Additional information as part of this update includes: project information sheets and status maps, the 5-year Capital Improvement Bond Program, and the current bond ordinance amendment. These are located at www.bonds.pima.gov

Pima County **BOND** 
PROGRAM Update

Completed Projects Summary

SEMI-ANNUAL REPORT FOR FISCAL YEAR 2008/2009



Green Valley Performing Arts Center



Rillito-Tucson Neighborhood



Canoa Ranch Building Rehabilitation



Interagency Victim Advocacy Center

Recently Completed Projects

During six months ending December 2008, there have been 34 projects and subprojects completed and seven open space acquisitions totaling \$58.5 million. The completed projects are listed by bond authorization and question number. For additional information on completed bond projects, refer to the Completed Bond Project Report at www.bonds.pima.gov/comproj.pdf.



Sands Ranch — Open Space Acquisition



Pima **BOND**

PROGRAM *Update*

Completed Projects Summary

SEMI-ANNUAL REPORT FOR FISCAL YEAR 2008/2009

Completed Projects

Six Months Ending December 2008

Bond Authorization	Q. No	Bond No	Project / Subproject Name	Completion	Cost (\$000)
1997 GO	3	P-05	Manuel Herrera Park Improvements (COT)	Oct-08	150
1997 GO	3	P-34	Oro Valley CDO River Park	Aug-08	1,000
1997 GO	3	P-46	Columbus Park	Dec-08	2,000
1997 GO	4	CH-29	Canoa Ranch Bldgs 103/105 Rehab (1997 Auth)	Dec-08	740
1997 GO	5	FS-13	ADA Facility Accessibility Projects	Dec-08	226
1997 GO	5	NR-16	Pueblo Gardens Elementary	Dec-08	138
1997 HURF	DOT	DOT-41	Park Villa Casitas	Nov-08	67
1997 HURF	DOT	DOT-57	Orange Grove/Silverbell Intersection Improvements	Nov-08	1,357
2004 GO	1	OS1.21	Sands Ranch	Dec-08	10,386
2004 GO	1	OS1.23	Sopori Ranch	Dec-08	10,331
2004 GO	2	FM2.06	Green Valley Performing Arts Center Phase 2	Dec-08	4,250
2004 GO	2	FM2.07	Mt. Lemmon Community Center	Aug-08	1,298
2004 GO	2	FM2.08	Amado Food Bank Kitchen	Aug-08	558
2004 GO	2	HR2.10	Sylvester Drive Estates	Aug-08	485
2004 GO	2	NR2.09	Highland Vista	Aug-08	75
2004 GO	2	NR2.09	Flowing Wells Health Clinic	Sep-08	500
2004 GO	3	FM3.02	Justice Court – State of Arizona Property	Aug-08	2,089
2004 GO	3	FM3.02	Justice Court – Rasmussen Ford - Helms Trust Property	Aug-08	641
2004 GO	3	FM3.02	Justice Cour – McCuistion Property	Aug-08	460
2004 GO	3	FM3.02	Justice Court – Stone-Toole LLC Property	Aug-08	1,419
2004 GO	3	FM3.04	Corrections Jail Security – Main Jail HVAC Improvements	Aug-08	307
2004 GO	3	FM3.04	Corrections Jail Security – Training Center/Support Services Remodel	Aug-08	1,507
2004 GO	3	FM3.05	Interagency Victim Advocacy Center	Oct-08	5,916
2004 GO	3	FM3.06	Juvenile Court – Central Plant Improvements	Aug-08	718
2004 GO	3	FM3.06	Juvenile Court – Tenant Improvements	Aug-08	1,264
2004 GO	4	CR4.02	Canoa Ranch Master Plan	Jul-08	400
2004 GO	4	CR4.02	Canoa Ranch Recon Bldg 106-109	Sep-08	1,000
2004 GO	4	CR4.04	San Pedro Chapel	Jul-08	500
2004 GO	4	CR4.12	Performing Arts Center Rehabilitation	Nov-08	682
2004 SR	6	SS6.01	Roger Rd WWTP Biotower Arm Replacement	Aug-08	827
2004 SR	6	SS6.01	Roger Road Odor Control Projects	Aug-08	7,180
